Ventilation Assessment Summary

Ventilation Assessment
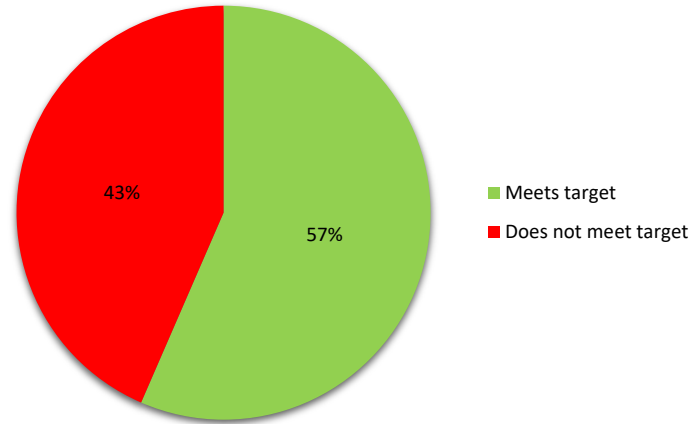
- Meets target — 57%
- Does not meet target — 43%

#	HVAC		Site		Air Changes			Recommendation	
	Room	Type	Campus	Building	Target	Actual	Result	Min. CADR	Min. Supply
1	L110	Break room	Laney College	Library	3	1.2	Does not meet target	303	564
2	L108	Occupiable Storage (L	Laney College	Library	3	10.8	Meets target	0	90
3	L114	Office	Laney College	Library	3	0.3	Does not meet target	553	685
4	L102	Office	Laney College	Library	3	3.6	Meets target	0	289
5	L104	Computer Lab	Laney College	Library	3	0.2	Does not meet target	431	507
6	L101	Computer Lab	Laney College	Library	3	1.1	Does not meet target	269	477
7	L109	Office	Laney College	Library	3	4.9	Meets target	0	413
8	L110A	Office	Laney College	Library	3	2.2	Does not meet target	10	44
9	L202	Office	Laney College	Library	3	3.1	Meets target	0	60
14	Stacks 2	Library	Laney College	Library	3	2.4	Does not meet target	1999	11453
15	L304	Conference	Laney College	Library	3	5.0	Meets target	0	63
16	L306	Conference	Laney College	Library	3	4.9	Meets target	0	63
17	L308	Conference	Laney College	Library	3	5.2	Meets target	0	63
18	L310	Conference	Laney College	Library	3	1.8	Does not meet target	24	63
19	L312	Conference	Laney College	Library	3	3.5	Meets target	0	130
20	L313	Conference	Laney College	Library	3	6.4	Meets target	0	63
21	L311	Conference	Laney College	Library	3	8.8	Meets target	0	64
22	L309	Conference	Laney College	Library	3	6.4	Meets target	0	64
23	L307	Office	Laney College	Library	3	5.0	Meets target	0	64
24	L305	Office	Laney College	Library	3	5.2	Meets target	0	133
27	Stacks 3	Library	Laney College	Library	3	2.3	Does not meet target	1159	5653

#	HVAC		Site		Air Changes			Recommendation	
	Room	Type	Campus	Building	Target	Actual	Result	Min. CADR	Min. Supply
28	L110B	Office	Laney College	Library	3	0.0	**Does not meet target**	39	43
29	L110C	Office	Laney College	Library	3	1.2	**Does not meet target**	97	183
